
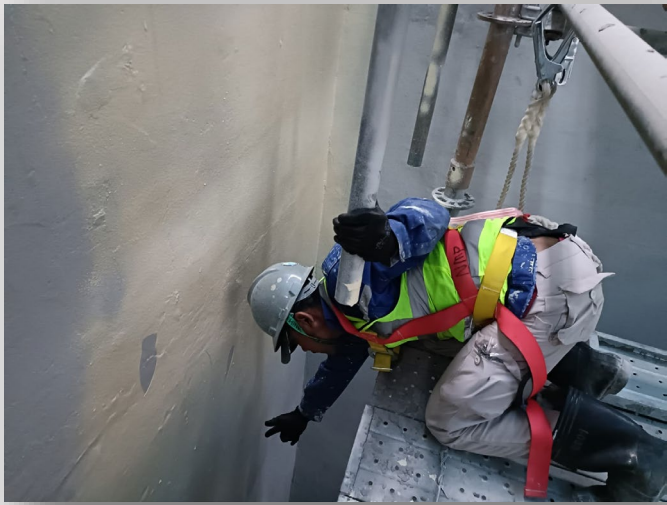




# Potential Fatal Event: Fall from Heights

Preliminary Incident Details	
Operation	Manyar Smelter – Desalination Plant
Date / Time	October 31, 2023 / 3:30 p.m.
Type	Injury
Summary	A subcontractor employee was applying coating on a tank from scaffolding and was reminded to tie off by a Health and Safety specialist. While attempting to stand up to tie off, the employee lost balance and fell through the gap about 4 meters (13 feet) to the ground.
Fatal Risk	Fall from Heights
Risk Category	Monitor
Risk Rating	Significant (3) Possible (2)
Findings / Missing Controls	<ul style="list-style-type: none"> <li>Employee was not tied off</li> </ul>
Applicable Policies / Procedures	<ul style="list-style-type: none"> <li><a href="#">Working at Heights policy</a></li> <li>Work procedures and training</li> </ul>
Employee Condition	The employee received a laceration requiring eight stitches above the right eye and was cleared to return to work.
Contact	Zach Scrivner, Manager-Corporate Project Engineering Safety

Photos / Links	
	<i>The scaffolding where the worker fell.</i>
	<i>Reenactment – The worker fell about four meters to the ground.</i>
